



## Haws Oregon Chub Enhancement Pond

OWEB Project #207-074  
Year One Monitoring Report



*Pre-Implementation: East hole; monitoring of water table levels indicates decrease of water elevation over time. May 2006*



*Pre-Implementation: West hole; indicates consistent water levels over time. May 2006*



*Pre-Implementation: Public receives tour of proposed project site. June 2007*



*Pre-implementation: Based on monitoring results, project redesigned for excavation of west side only. June 2007*



*Implementation: Project begins with clearing of site and pond excavation: August 2007*



*Implementation: Landowner, Eric Haws and Contractor watch as the excavation of earth begins. August 2007*



*Implementation: Excavator removes earth to create 1.8 meter depth pond for Oregon chub. August 2007*




*Implementation: 500 square meter pond excavated to create off-channel habitat for Oregon chub.*



*Implementation: 500 square by 1.8 meter pond with sloped banks. August 2007.*



*Implementation: Satisfied landowner.*

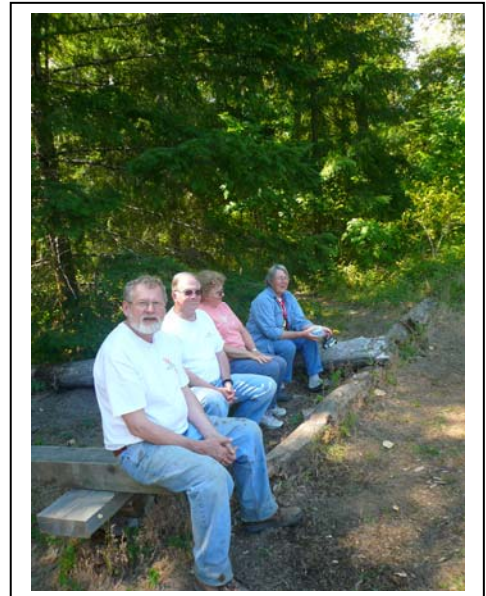

*Implementation: Project brought neighbors together. August 2007*



*Post Implementation: Slopes are stabilized with native planting of Elymus Glaucus. October 2007*




*Post-Implementation: Elymus Glaucus established on slopes, providing bank stabilization. March 2008.*



*Post-Implementation: Water levels are stable. March 2008*



*Post-Implementation: Aquatic vegetation plugs examined for establishment. March 2008*

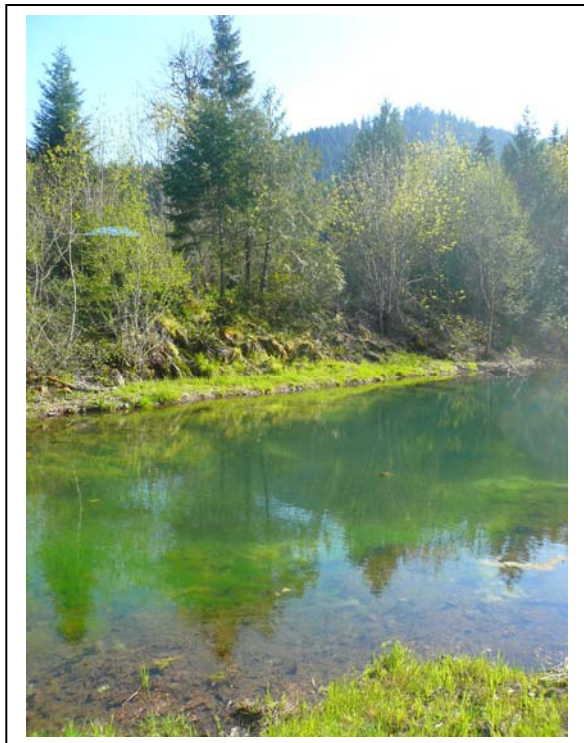

*Post-Implementation: Water levels, aquatic vegetation and riparian grasses and trees healthy. May 2008*

